JUNE 1924
UNION BRIDGE
MD.

(1631)

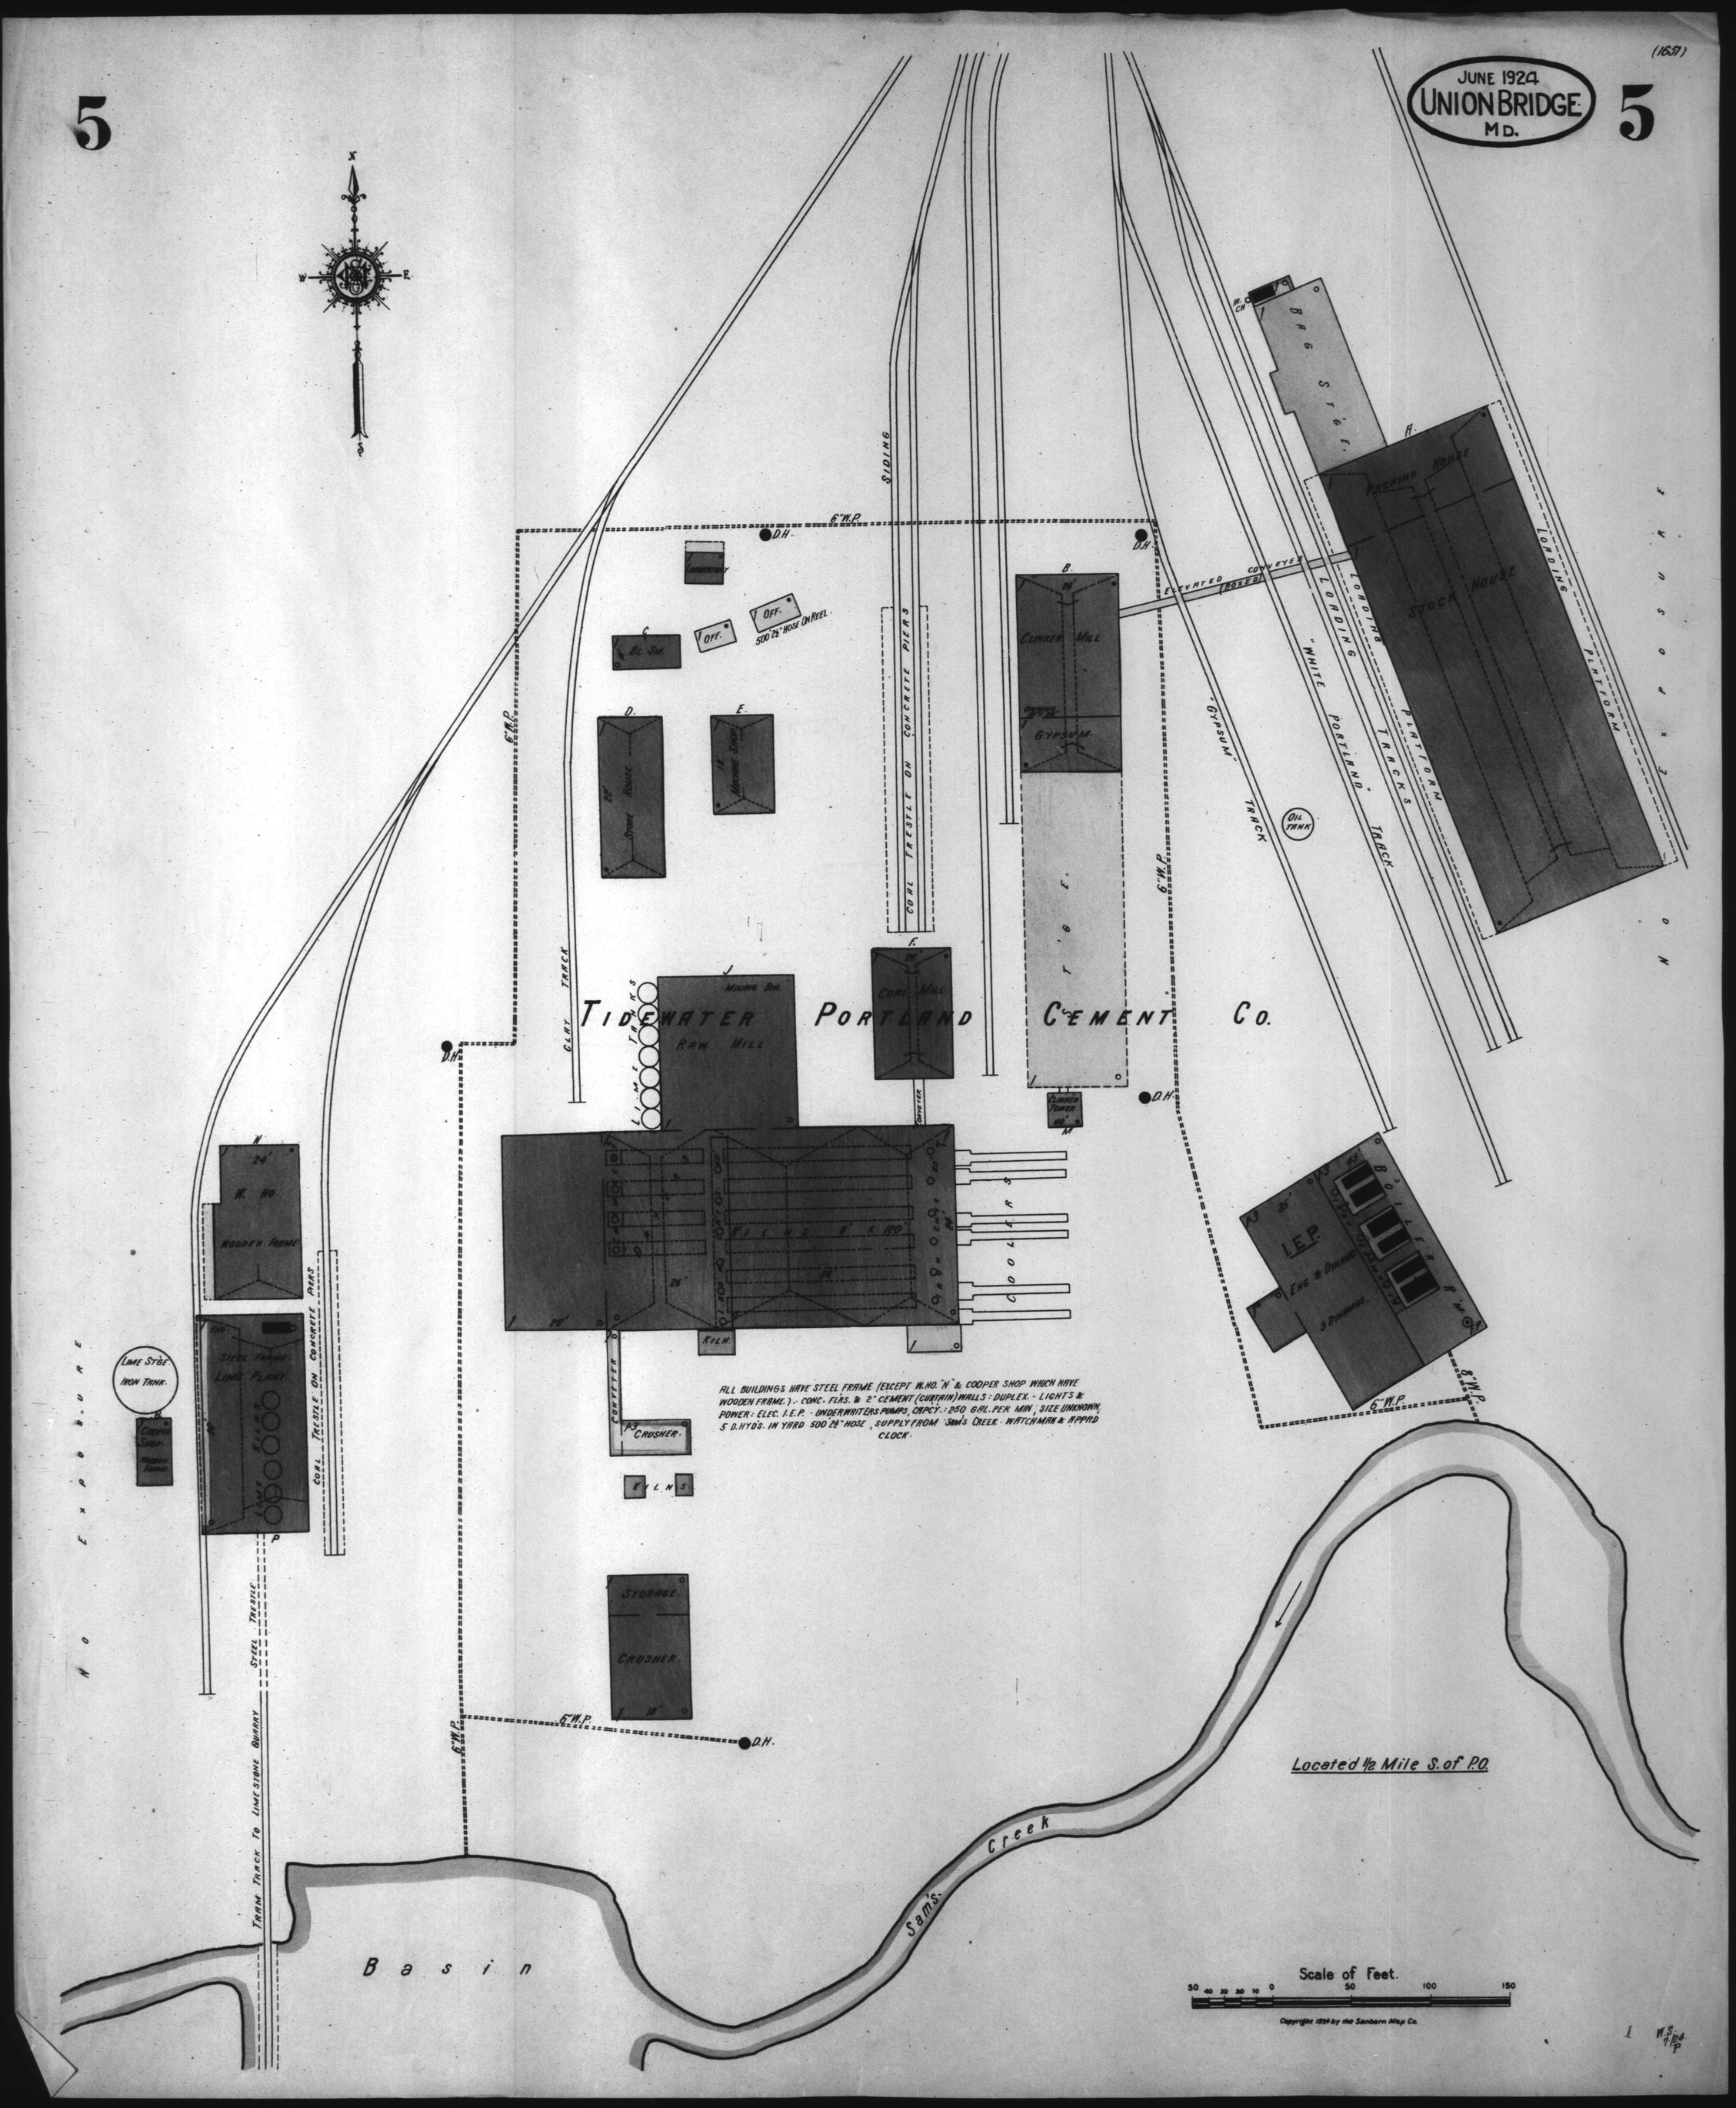

ALL BUILDINGS HAVE STEEL FRAME (EXCEPT W.HO. "N" & COOPER SHOP WHICH HAVE WOODEN FRAME.) - CONC. FLRS. & 2" CEMENT (CURTAIN) WALLS: DUPLEX. - LIGHTS & POWER: ELEC. I.E.P. - UNDERWRITERS PUMPS, CAPCY.: 250 GAL. PER MIN, SIZE UNKNOWN, 5 D.HYD'S. IN YARD 500 2½" HOSE, SUPPLY FROM SAM'S CREEK. - WATCHMAN & APPRD CLOCK.
