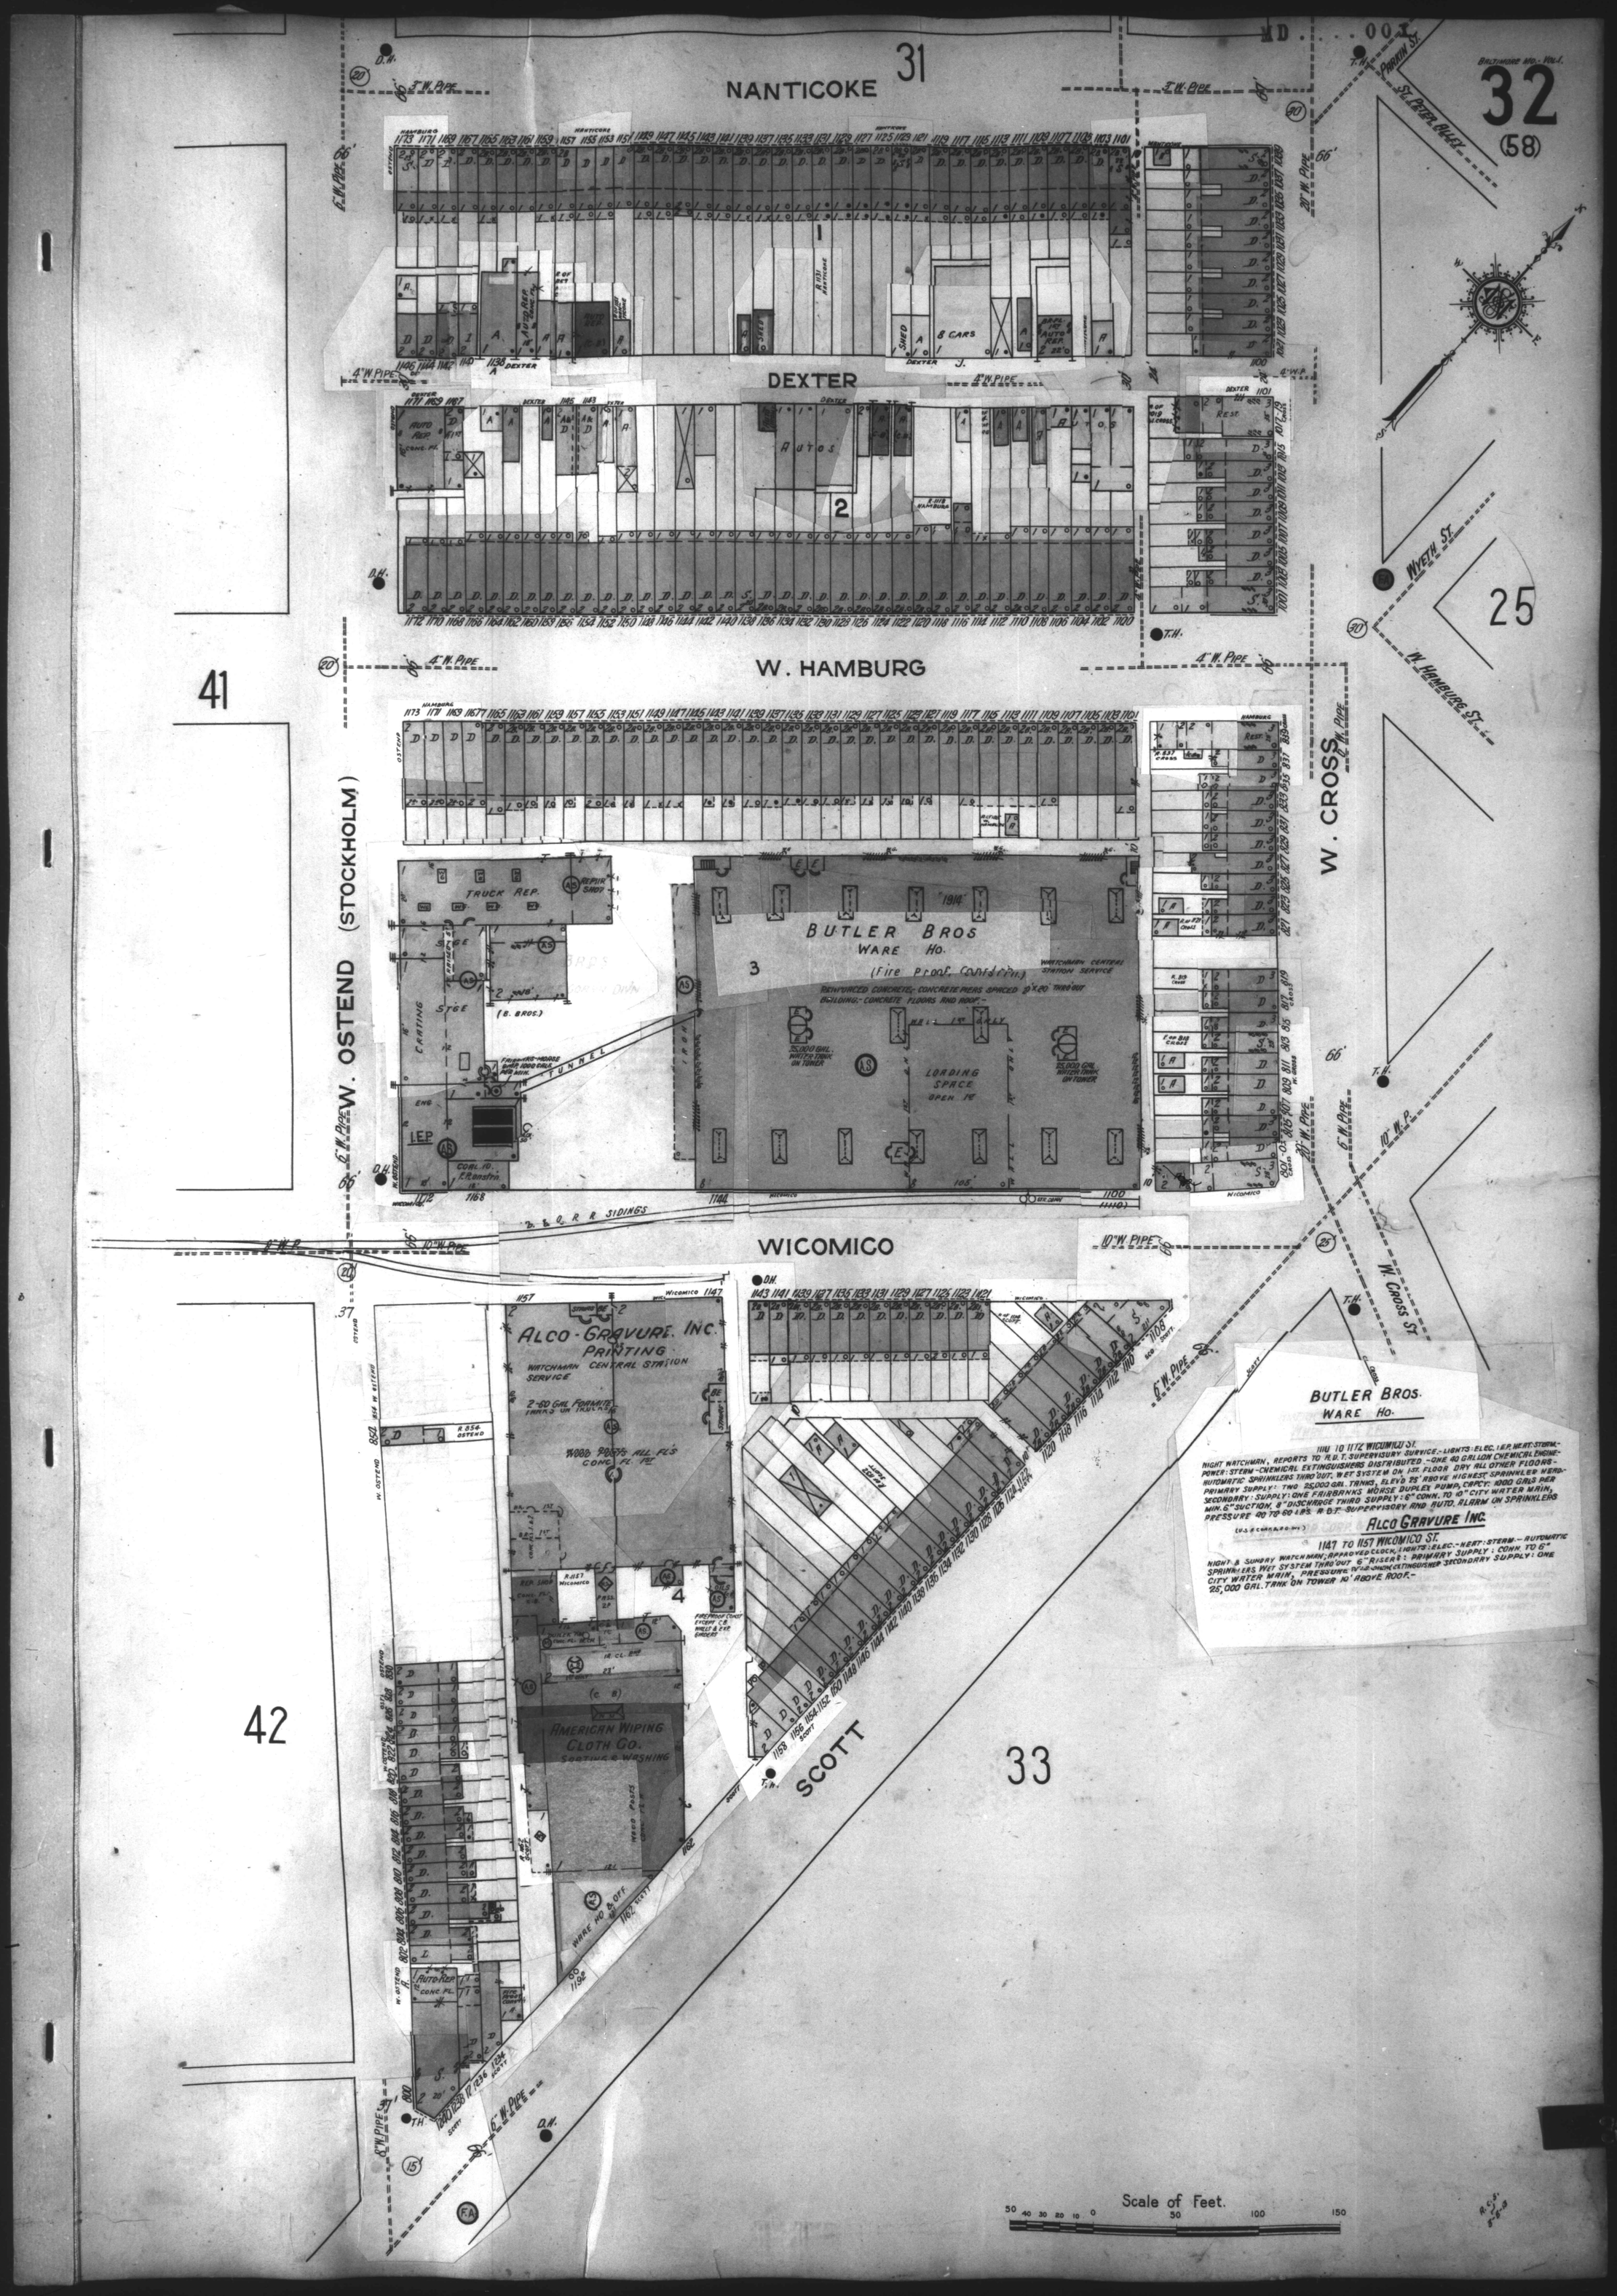
NANTICOKE
31
DEXTER
W. HAMBURG
W. OSTEND (STOCKHOLM)
W. CROSS
WICOMICO
SCOTT
32
(58)
25
33
41
42
PARKIN ST.
ST. PETER ALLEY
WYETH ST.
W. HAMBURG ST.
W. CROSS ST.
TRUCK REP.
REPAIR SHOP
STAGE
CARTING
I.E.P.
TUNNEL
BUTLER BROS
WARE HO.
(Fire Proof Construction)
WATCHMAN CENTRAL STATION SERVICE
REINFORCED CONCRETE; CONCRETE PIERS SPACED 23'X20' THRO'OUT
BUILDING:- CONCRETE FLOORS AND ROOF.-
25,000 GAL. WATER TANK ON TOWER
LOADING SPACE
OPEN TO
B. & O. R. R. SIDINGS
ALCO-GRAVURE, INC.
PRINTING
WATCHMAN CENTRAL STATION SERVICE
2-60 GAL FORMITE TANKS ON TROLLEYS
WOOD POSTS ALL FL'S
CONC. FL. 1ST
AMERICAN WIPING CLOTH CO.
SORTING & WASHING
WARE HO. & OFF.
AUTO REP.
CONC. FL.
BUTLER BROS.
WARE HO.
1110 TO 1112 WICOMICO ST.
NIGHT WATCHMAN, REPORTS TO N.D.T. SUPERVISORY SERVICE.- LIGHTS: ELEC. I.E.P. HEAT: STEAM.- POWER: STEAM - CHEMICAL EXTINGUISHERS DISTRIBUTED. - ONE 40 GALLON CHEMICAL ENGINE- AUTOMATIC SPRINKLERS THRO'OUT. WET SYSTEM ON 1ST. FLOOR DRY ALL OTHER FLOORS - PRIMARY SUPPLY: TWO 25,000 GAL. TANKS, ELEV'D 25' ABOVE HIGHEST SPRINKLER HEAD.- SECONDARY SUPPLY: ONE FAIRBANKS MORSE DUPLEX PUMP, CAPCY: 1000 GALS PER MIN. 6" SUCTION, 8" DISCHARGE THIRD SUPPLY: 6" CONN. TO 10" CITY WATER MAIN, PRESSURE 40 TO 60 LBS. N.D.T. SUPERVISORY AND AUTO. ALARM ON SPRINKLERS
ALCO GRAVURE INC.
1147 TO 1157 WICOMICO ST.
NIGHT & SUNDAY WATCHMAN; APPROVED CLOCK, LIGHTS: ELEC.- HEAT: STEAM - AUTOMATIC SPRINKLERS, WET SYSTEM THRO'OUT 6" RISERS: PRIMARY SUPPLY: CONN. TO 6" CITY WATER MAIN, PRESSURE 15 LBS. HAND EXTINGUISHER SECONDARY SUPPLY: ONE 25,000 GAL. TANK ON TOWER 10' ABOVE ROOF.-
Scale of Feet.
50 40 30 20 10 0 50 100 150
